
MEMORANDUM

TO: Boulder County Communications – bsocommunications@bouldercounty.org
Boulder Valley School District Transportation – transportation@bvsvd.org
City of Louisville Fire District – jhenderson@louisvillefire.com
City of Louisville Police Department – Rafael Gutierrez, Police Chief
City of Louisville City Manager's Office, City of Louisville Communications
City of Louisville Public Works Director – Kurt Kowar
City of Louisville Public Works Operations – Ben Francisco
City of Louisville Public Works Facilities – Kevin Frey
City of Louisville Parks & Recreation – Adam Blackmore, Director Pks & Rec
City of Louisville Parks & Recreation – Abby McNeal, Parks Superintendent
City of Louisville Coal Creek Golf Course – David Dean, Superintendent
City of Louisville Planning Department – Rob Zuccaro, Planning Director
Republic Services – sroundy@republicservices.com
RTD – engineering@rtd-denver.com; michelle.sims@rtd-denver.com

FROM: Michael O'Keefe: Engineering Technician for City of Louisville Public Works



DATE: Thursday, April 24, 2025

RE: Road Closure: Summit View Dr. (Kaylix Ave. to Hwy. 42)

Stone and Concrete, a contractor being utilized by City of Louisville, will be removing and replacing damaged concrete in Summit View Dr. right-of-way. The current schedule for work is from Monday, April 28 to Thursday, May 8.

A detour to the north on Kaylix Ave. and Paschal Dr. will be established. A detour to the south on W Hecla Dr. will also be set up. The Front Range Eye Health Center will only be accessible from the west on Summit View Dr. near the intersection with Kaylix Ave. Site and traffic control plans can be seen on the following pages. Please feel free to reach out to me with any comments or questions.

Thank you.

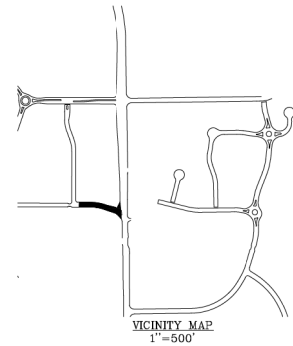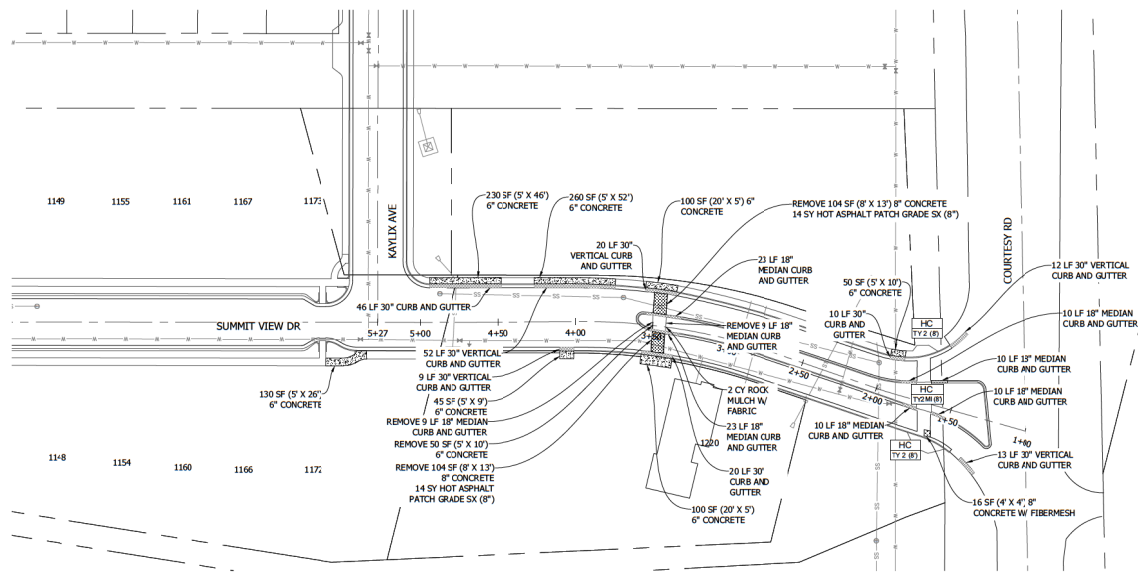

NOTES


1. CONCRETE INDICATED ON THIS SHEET SHALL BE REMOVED AND REPLACED UNLESS OTHERWISE NOTED.
2. PROVIDE #4 REBAR, CONTINUOUS, 18\"
3. PROVIDE #4 SMOOTH REBAR DOWELS (18\"
4. CONTRACTOR SHALL PROVIDE ASPHALT PATCH 2' WIDE, ADJACENT TO CURBWALK / CURB REPLACEMENT AS REQUIRED BY THE ENGINEER.
5. CONTRACTOR SHALL NOTIFY ALL RESIDENTS AND BUSINESSES WITHIN WORK AREA AT A MINIMUM OF 5 BUSINESS DAYS IN ADVANCE.
6. CONTRACTOR SHALL VIDEO OR PHOTOGRAPH EXISTING CONDITIONS AT A MINIMUM OF 5 DAYS IN ADVANCE AND PROVIDE CITY OF LOUISVILLE WITH COPIES.


FOOTNOTES:

- SEE ADA RAMP DETAILS.

QUANTITY SUMMARY		
ITEM	UNIT	QUANTITY
ROCK MULCH W/ FABRIC	CY	2
REMOVE 18\"	LF	18
REMOVE 6\"	SF	50
REMOVE 8\"	SF	208

QUANTITY SUMMARY		
ITEM	UNIT	QUANTITY
18\"	LF	86
30\"	LF	182
6\"	SF	915
8\"	SF	16
HOT ASPHALT PATCH GRADE SX (8\")	SY	45
RAMP TY 2 (8\")	EA	2
RAMP TY 2 MI (8\")	EA	1



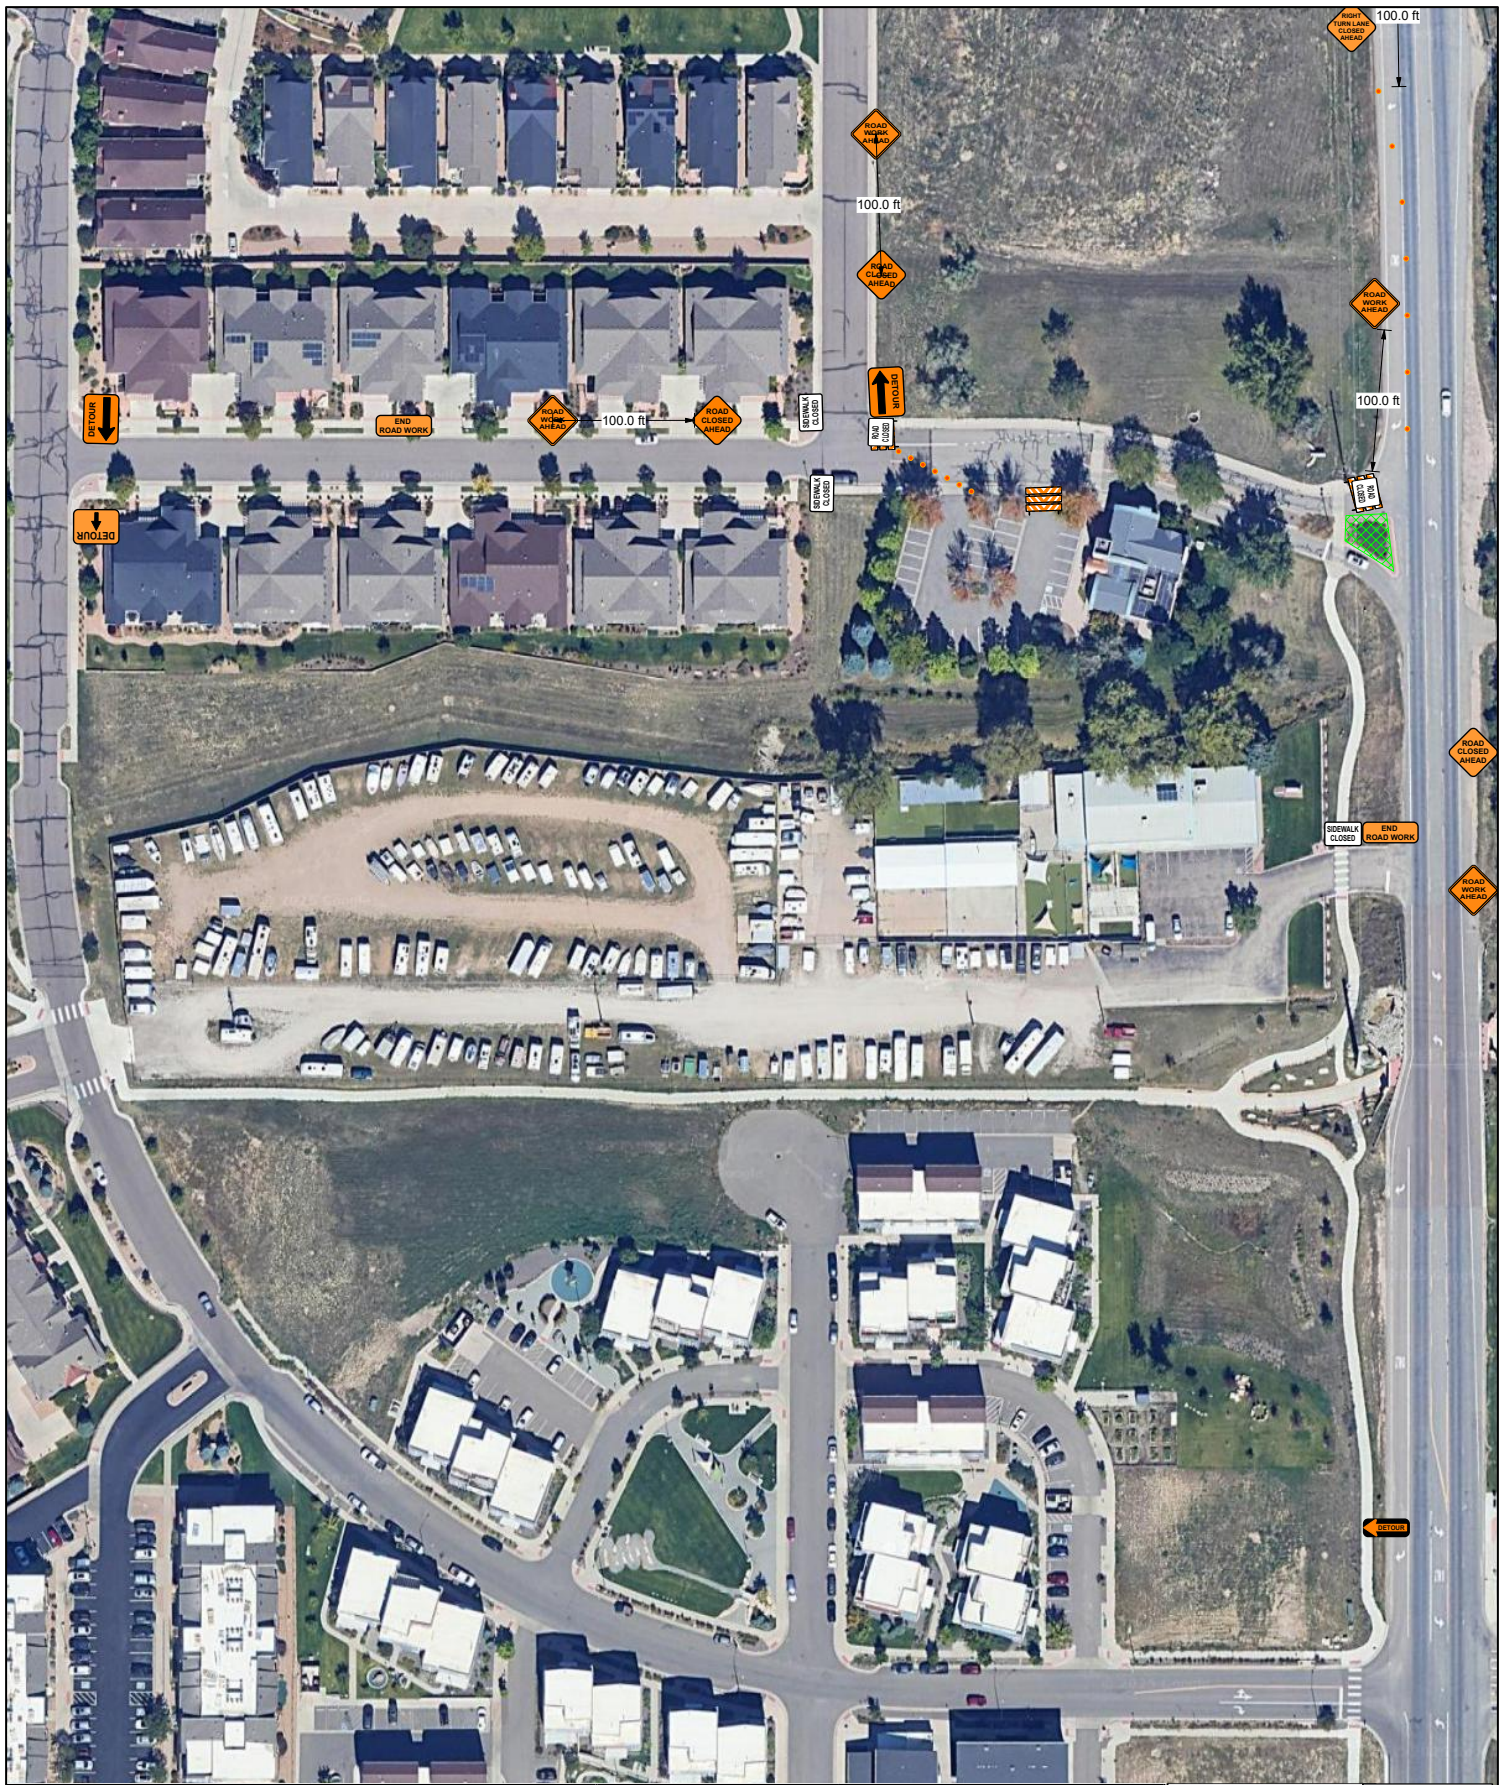

PREPARED BY:



PROJECT: 2025 Concrete Replacement Project

NOTES: Road Closed

PLAN No: 0059

DATE: TBD

DRAWN BY: Eduardo Marquez

REVISION: Eduardo Marquez

LICENSE No ATTSA Card Provided

Manifest

14 x Barrel
 4 x W20-1F
 3 x ??
 3 x R9-9
 2 x G20-2a
 2 x M4-9
 2 x R11-2
 2 x W20-3
 1 x CW20-3
 1 x M4-10
 1 x M4-10D

Legend

